

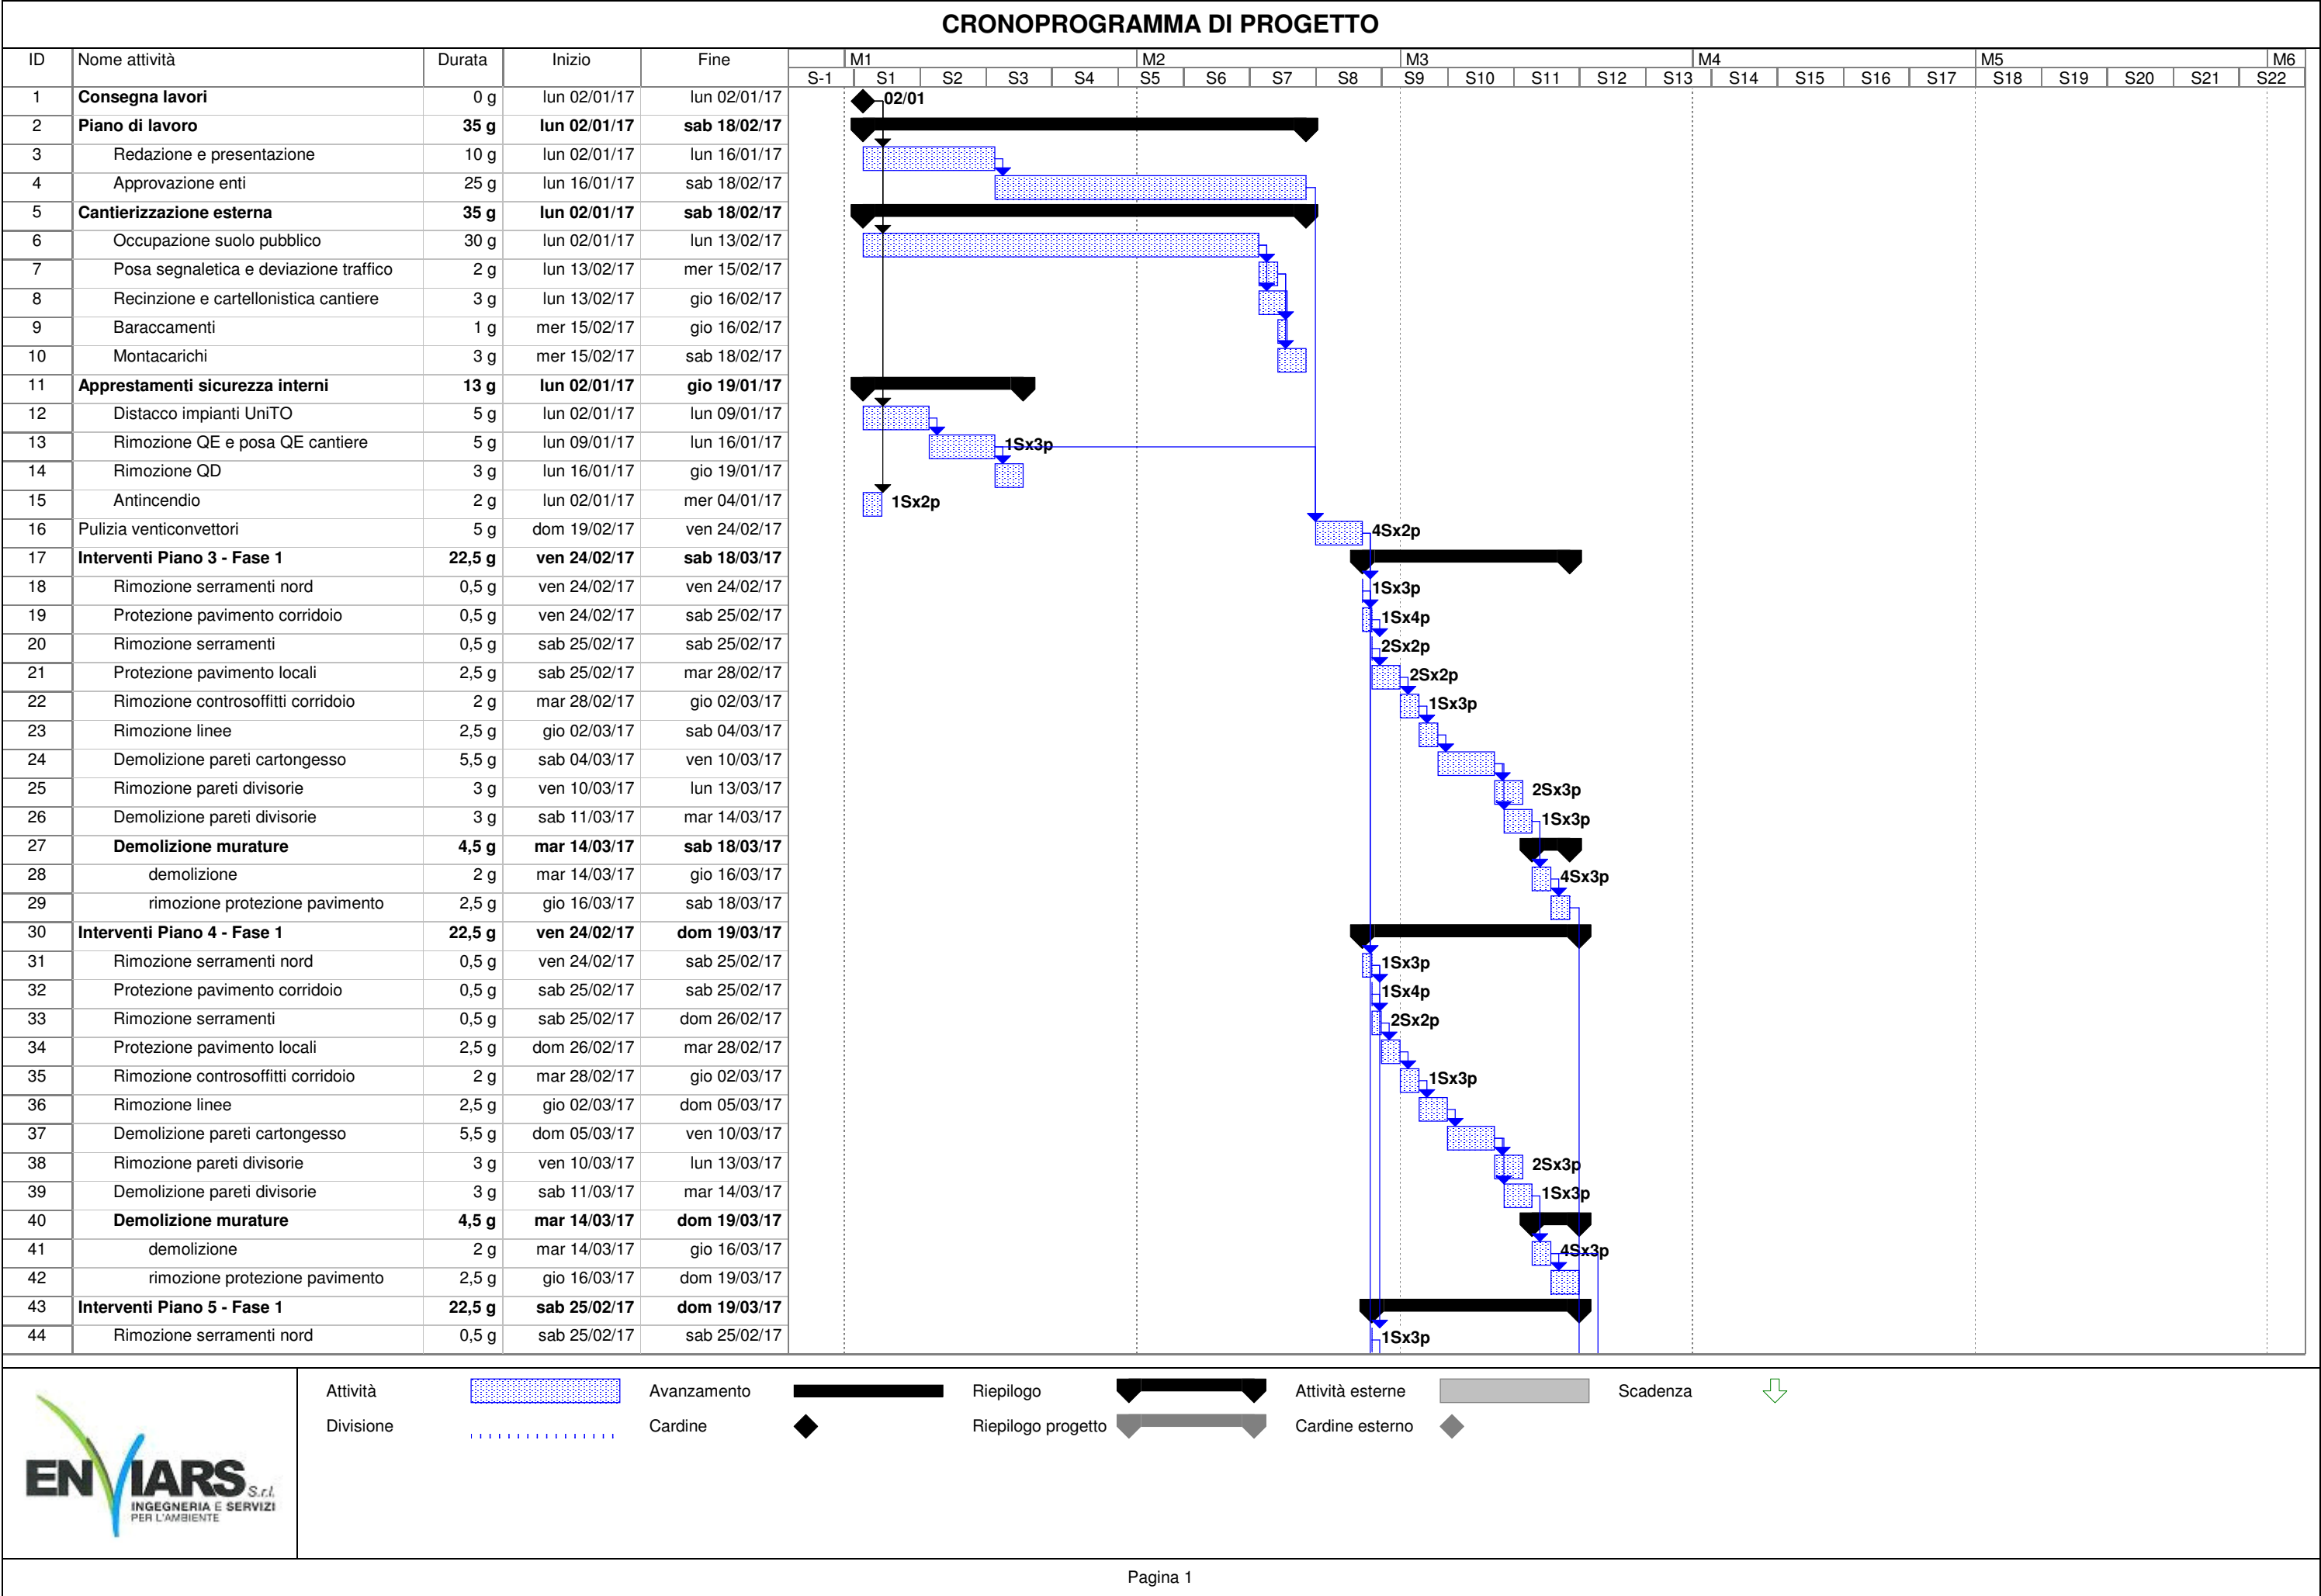
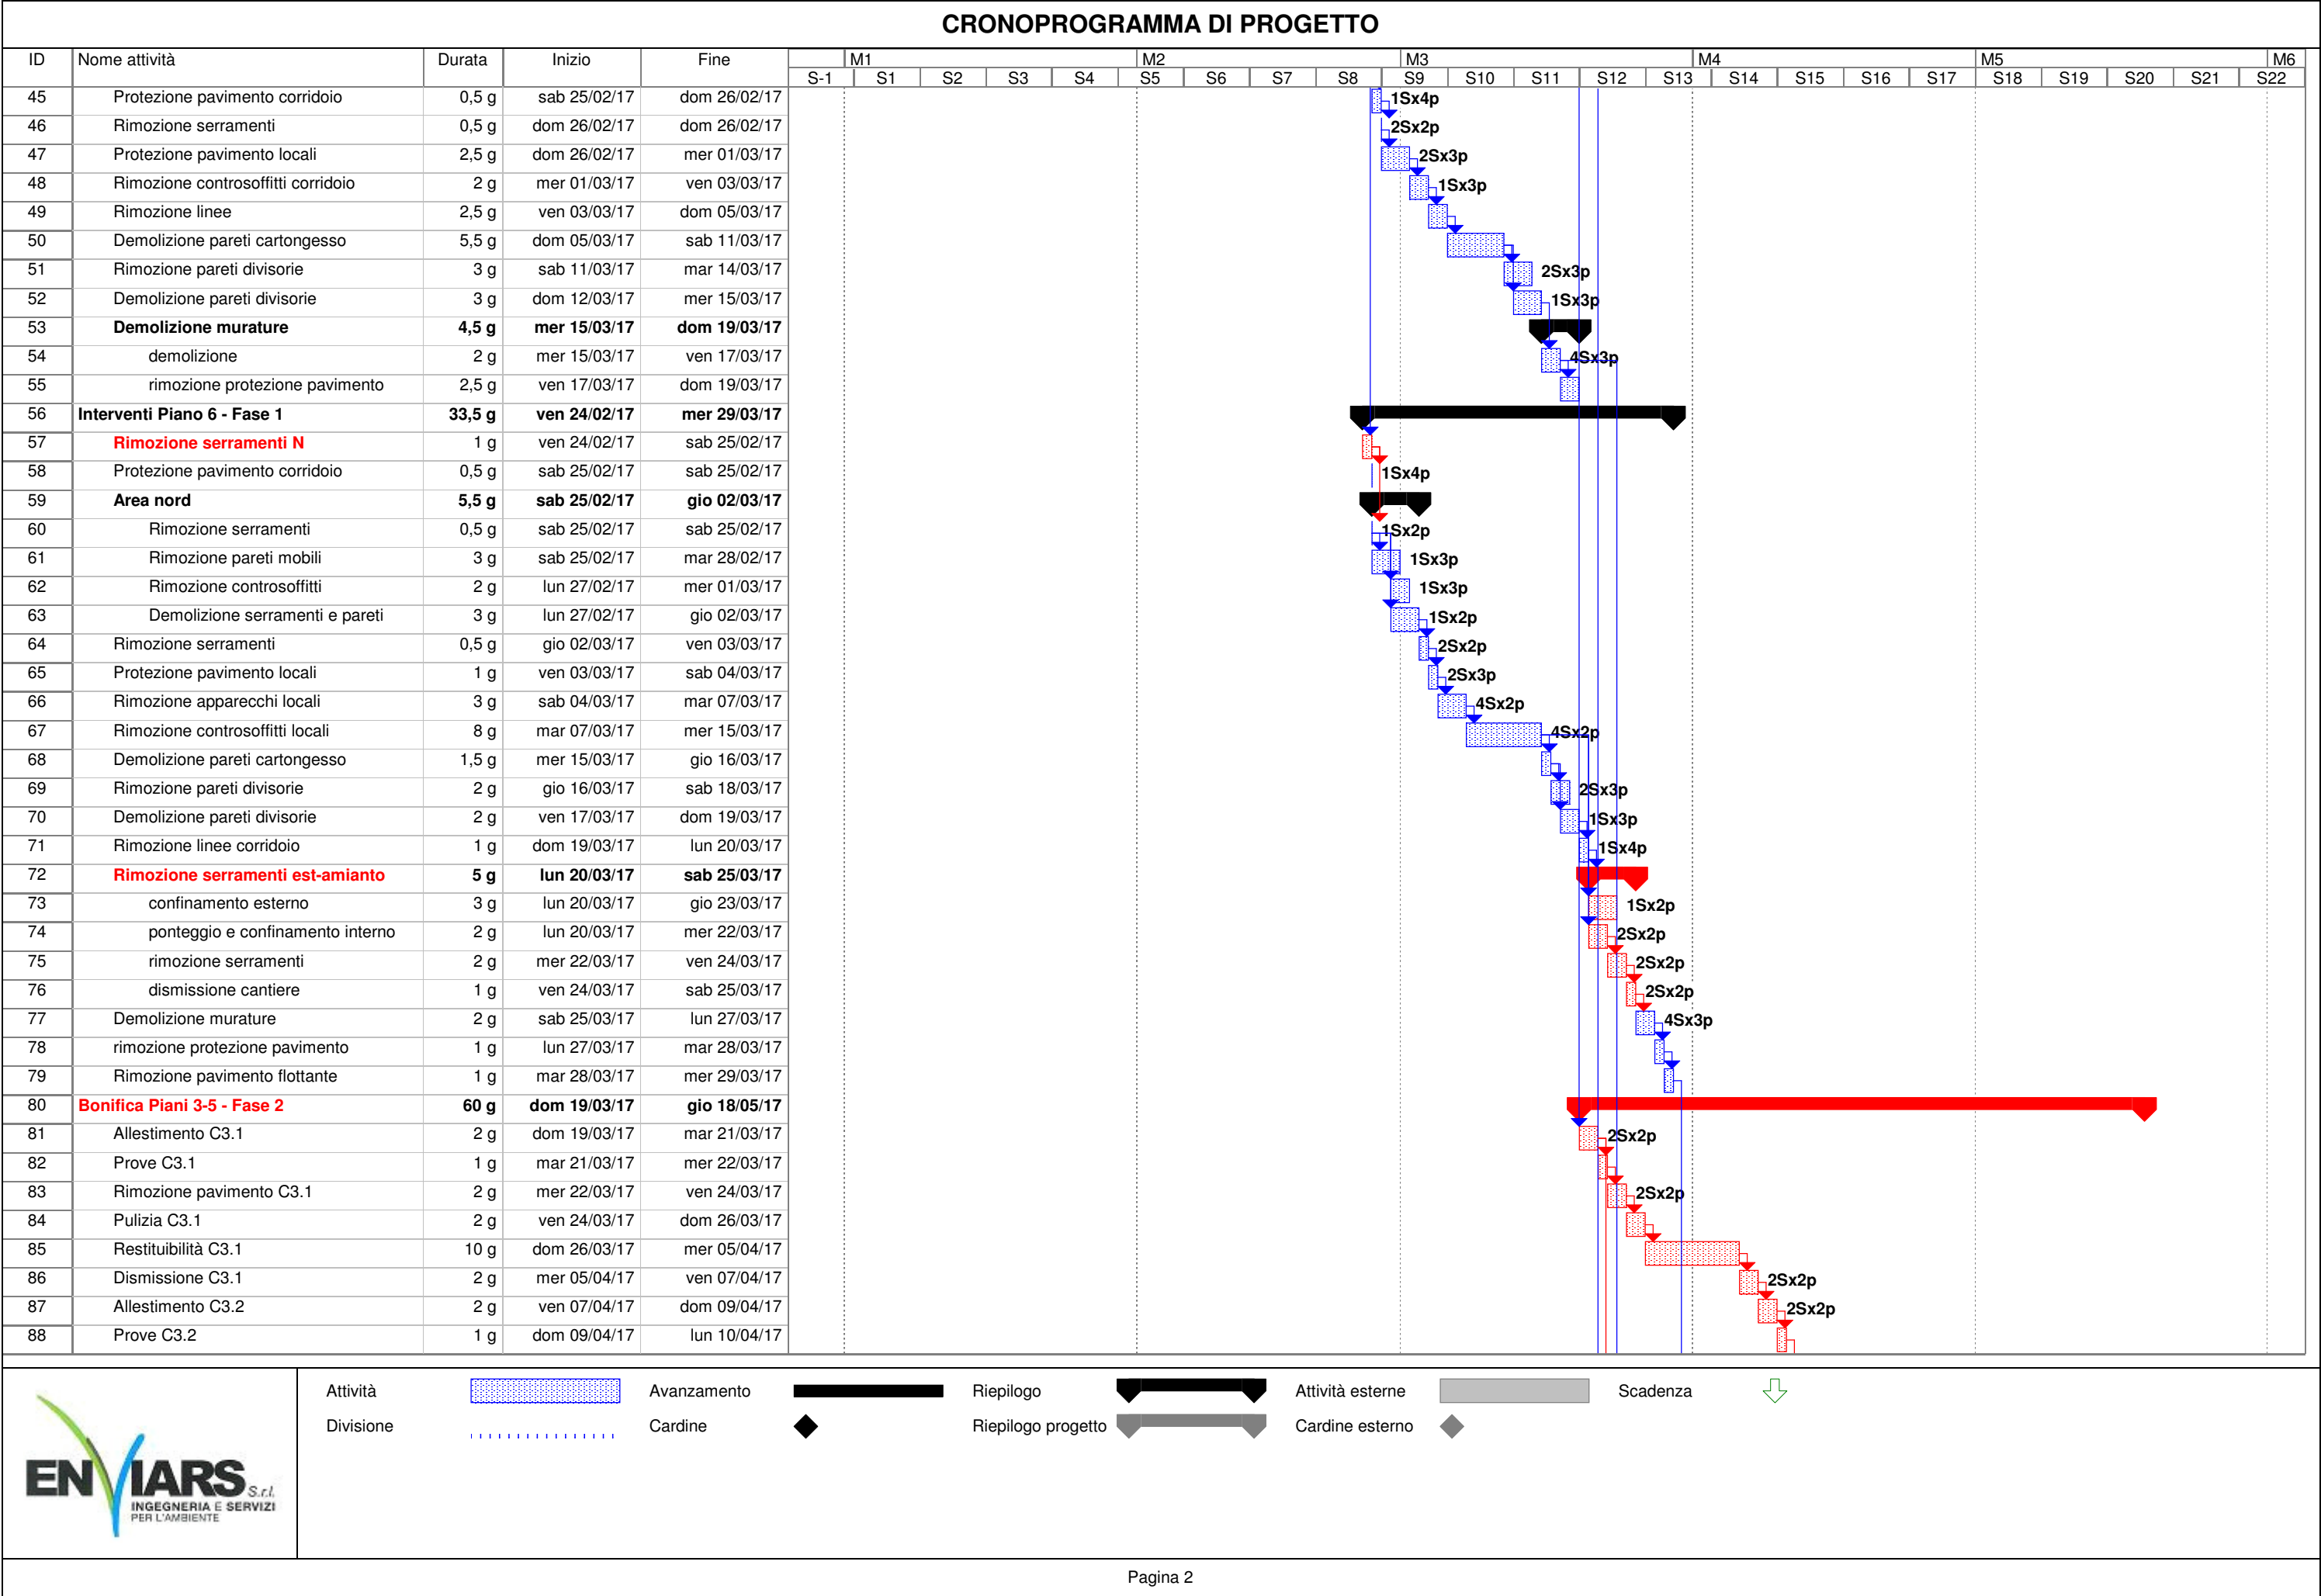






CRONOPROGRAMMA DI PROGETTO																											
ID	Nome attività	Durata	Inizio	Fine		M1					M2				M3			M4					M5				M6
					S-1	S1	S2	S3	S4	S5	S6	S7	S8	S9	S10	S11	S12	S13	S14	S15	S16	S17	S18	S19	S20	S21	S22
89	Rimozione pavimento C3.2	2 g	lun 10/04/17	mer 12/04/17																							
90	Pulizia C3.2	2 g	mer 12/04/17	ven 14/04/17																							
91	Restituibilità C3.2	10 g	ven 14/04/17	lun 24/04/17																							
92	Dismissione C3.2	2 g	lun 24/04/17	mer 26/04/17																							
93	Allestimento C3.3	2 g	mer 26/04/17	ven 28/04/17																							
94	Prove C3.3	1 g	ven 28/04/17	sab 29/04/17																							
95	Rimozione pavimento C3.3	2 g	sab 29/04/17	lun 01/05/17																							
96	Pulizia C3.3	2 g	lun 01/05/17	mer 03/05/17																							
97	Restituibilità C3.3	10 g	mer 03/05/17	sab 13/05/17																							
98	Dismissione C3.3	2 g	sab 13/05/17	lun 15/05/17																							
99	Allestimento C4.1	2 g	mar 21/03/17	gio 23/03/17																							
100	Prove C4.1	1 g	gio 23/03/17	ven 24/03/17																							
101	Rimozione pavimento C4.1	2 g	ven 24/03/17	dom 26/03/17																							
102	Pulizia C4.1	2 g	dom 26/03/17	mar 28/03/17																							
103	Restituibilità C4.1	10 g	mar 28/03/17	ven 07/04/17																							
104	Dismissione C4.1	2 g	ven 07/04/17	dom 09/04/17																							
105	Allestimento C4.2	2 g	dom 09/04/17	mar 11/04/17																							
106	Prove C4.2	1 g	mar 11/04/17	mer 12/04/17																							
107	Rimozione pavimento C4.2	2 g	mer 12/04/17	ven 14/04/17																							
108	Pulizia C4.2	2 g	ven 14/04/17	dom 16/04/17																							
109	Restituibilità C4.2	10 g	dom 16/04/17	mer 26/04/17																							
110	Dismissione C4.2	2 g	mer 26/04/17	ven 28/04/17																							
111	Allestimento C4.3	2 g	ven 28/04/17	dom 30/04/17																							
112	Prove C4.3	1 g	dom 30/04/17	lun 01/05/17																							
113	Rimozione pavimento C4.3	2 g	lun 01/05/17	mer 03/05/17																							
114	Pulizia C4.3	2 g	mer 03/05/17	ven 05/05/17																							
115	Restituibilità C4.3	10 g	ven 05/05/17	lun 15/05/17																							
116	Dismissione C4.3	2 g	lun 15/05/17	mer 17/05/17																							
117	Allestimento C5.1	2 g	gio 23/03/17	sab 25/03/17																							
118	Prove C5.1	1 g	sab 25/03/17	dom 26/03/17																							
119	Rimozione pavimento C5.1	2 g	dom 26/03/17	mar 28/03/17																							
120	Pulizia C5.1	2 g	mar 28/03/17	gio 30/03/17																							
121	Restituibilità C5.1	10 g	gio 30/03/17	dom 09/04/17																							
122	Dismissione C5.1	2 g	dom 09/04/17	mar 11/04/17																							
123	Allestimento C5.2	2 g	mar 11/04/17	gio 13/04/17																							
124	Prove C5.2	1 g	gio 13/04/17	ven 14/04/17																							
125	Rimozione pavimento C5.2	2 g	ven 14/04/17	dom 16/04/17																							
126	Pulizia C5.2	2 g	dom 16/04/17	mar 18/04/17																							
127	Restituibilità C5.2	10 g	mar 18/04/17	ven 28/04/17																							
128	Dismissione C5.2	2 g	ven 28/04/17	dom 30/04/17																							
129	Allestimento C5.3	1 g	dom 30/04/17	lun 01/05/17																							
130	Prove C5.3	2 g	lun 01/05/17	mer 03/05/17																							
131	Rimozione pavimento C5.3	1 g	mer 03/05/17	gio 04/05/17																							
132	Pulizia C5.3	2 g	gio 04/05/17	sab 06/05/17																							

	Attività		Avanzamento		Riepilogo		Attività esterne		Scadenza	
	Divisione		Cardine		Riepilogo progetto		Cardine esterno			

Pagina 3

